



Prime Consultant:		CITY OF POMPANO BEACH	GO BOND DIRECTOR:	HORACIO DANOVICH
Construction Manager at Risk:		CURRENT PHASE: CONSTRUCTION		
		DESIGN TEAM:	KEITH & ASSOCIATES	FEES: \$448,000.00
		CONSTRUCTION TEAM:	WHITING-TURNER	PRE-CONSTRUCTION FEES: \$83,025.00
		CONSTRUCTION TEAM:	WHITING-TURNER	CONSTRUCTION FEES: TBD
		AVAILABLE FUNDS:		TBD
		APPROVED BUDGET:	(Phase 1)	\$5,700,000.00

PROJECT OBJECTIVES

This project is the continuation of Dr. Martin Luther King Boulevard Jr. reconstruction within the downtown area. The planned improvements (for Phase 2)from NW 6th Avenue to NW 10 Avenue (I-95), will include paving, related drainage and water and sewer facilities within streets, sidewalks, medians, lighting, landscaping, street furniture and other streetscape improvements.

PROJECT UPDATES

Steady progress throughout July with only minor issues (gas pipe conflicts and unforeseen 48" pipes at NW 8th Ave). W-T completed the installation of the new 12" watermain and related service laterals between project limits. During the same period , drainage structures on Canal Street have been installed and conflict structure MH-6 set near NW 9th Avenue. Curb demolition and minor site investigation of the 2- unforeseen 48" drainage RCP near NW 8th Ave took place. A resolution of the issue and the conflict with MH 15 reviewed. Project is on schedule except for a 3-day hurricane delay. No significant issue aside from minor traffic challenges at NW 6th ave intersection which have been addressed with MOT in discussions with BSO. In November, roadway restoration of Westbound lane between NW 10th avenue and Canal street continues, and partial subgrade restoration up to NW 7th avenue is proceeding. Partial hardscape work, concrete sidewalk and curb were also performed. The first samples of soil cells were constructed and approved by the building department. Additionally, Drainage structures and electrical installation near completion for Westbound lane. Except for a storm rain event and minor changes to the work (conflicts and omissions), the project is on budget. Project schedule has only 11 impacted days to date including 2 tropical storms. Coordination is ongoing with BSO and local businesses to minimize impacts during construction. MOT in place for the westbound lanes and affected areas. **Project is on schedule and completion expected by July 2021. Scope includes demolition, water connections, installation of drainage structures, electrical conduits, irrigation sytem and subgrade restoration. Phased curb work and sidewalks completed.**

PROJECT FORECAST

Eastbound lane closed January 4, 2021 for Phase 4 work. Asphalt milling, drainage work and grouting of the abandoned watermain performed. **Phase 4 work including lighting, irrigation, flatwork, landscaping continues. The project remains on schedule to be completed by July 2021.**



PROJECT SCHEDULE

DESIGN / PERMITTING PHASE: Began May 2019 Ended: May 2020

CONSTRUCTION PHASE: JULY 2020 - JULY 2021

JUNE JULY AUG SEPT OCT NOV DEC JANUARY FEB MARCH APRIL MAY JUNE JULY AUG SEPT

PROJECT SITE LOCATION

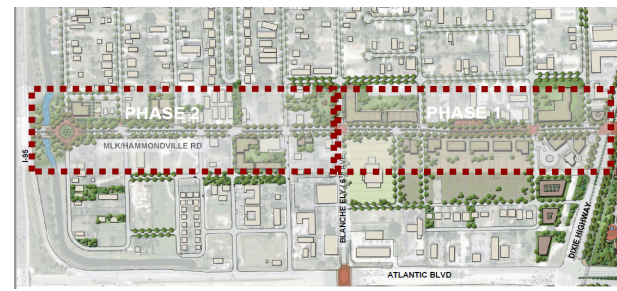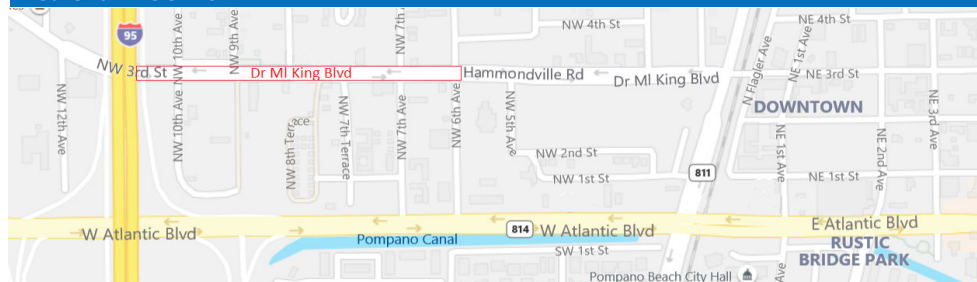

MLK BLVD. – PHASE 2

PROJECT FEATURES – COMPLETED PHASE 1 (EAST OF NW 6th AVENUE)

