



Prime Consultant:		CITY OF POMPANO BEACH	GO BOND DIRECTOR:	HORACIO DANOVIH
Construction Manager at Risk:		CURRENT PHASE: CONSTRUCTION		
		DESIGN TEAM:	KEITH & ASSOCIATES	FEES: \$448,000.00
		CONSTRUCTION TEAM:	WHITING-TURNER	PRE-CONSTRUCTION FEES: \$83,025.00
		CONSTRUCTION TEAM:	WHITING-TURNER	CONSTRUCTION FEES: TBD
		AVAILABLE FUNDS:		TBD
		APPROVED BUDGET:	(Phase 1)	\$5,700,000.00

PROJECT OBJECTIVES

This project is the continuation of Dr. Martin Luther King Boulevard Jr. reconstruction within the downtown area. The planned improvements (for Phase 2) from NW 6th Avenue to NW 10 Avenue (I-95), will include paving, related drainage and water and sewer facilities within streets, sidewalks, medians, lighting, landscaping, street furniture and other streetscape improvements.

PROJECT UPDATES

PROJECT FORECAST

Phase 4 work activities will continue with activation of lighting poles and installation of irrigation planting. Pavement restoration of Southbound lanes to also begin. The project remains on schedule to be completed by July 2021.



PROJECT SCHEDULE

DESIGN /PERMITTING PHASE: Began May 2019 Ended: May 2020

CONSTRUCTION PHASE: JULY 2020 - JULY 2021

JUNE JULY AUG SEPT OCT NOV DEC JANUARY

PROJECT SITE LOCATION

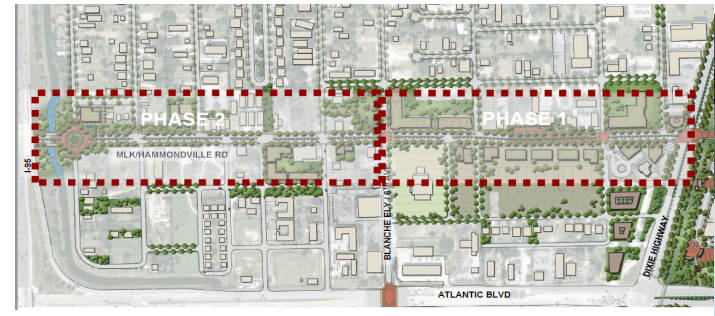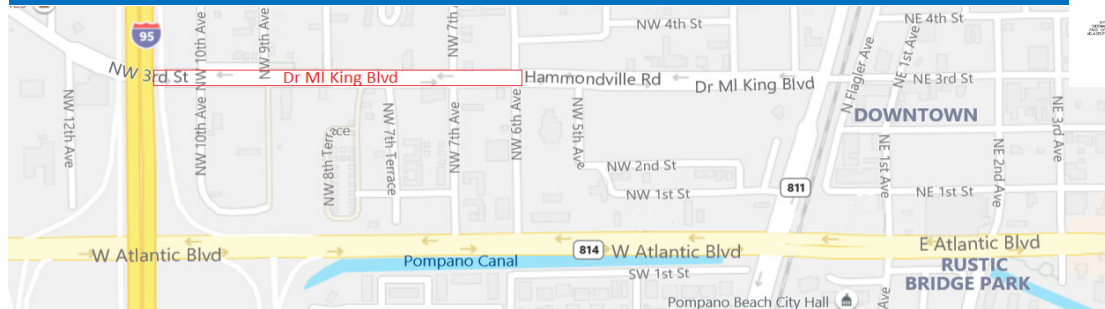

MLK BLVD. – PHASE 2

PROJECT FEATURES – COMPLETED PHASE 1 (EAST OF NW 6th AVENUE)

